CONFIDENTIAL · CLIENT REPORT

Engagement Update
Month 1 of 16

CEEFM Kft · BridgeWorks

Period: Weeks 1-5, late March to 30 April 2026

Issued: 2026-04-30

Prepared for
Victor Danmagaji
Managing Director, CEEFM Kft

Prepared by
Emmanuel Ehigbai
BridgeWorks · office@bridgeworks.agency

Period: Weeks 1-5 (late March to 30 April 2026)

Client: CEEFM Kft

Engagement: CEEFM-PROP-001 · 16-Week Digital Growth Programme

For: Victor Danmagaji, Managing Director

From: Emmanuel Ehigbai, BridgeWorks

Issued: 2026-04-30

At a Glance

- **GEO / AI Visibility Score:** 16 → 74 across Month 1. +58 points. From Critical to the top of the Fair band, one point shy of Good.
- **Marketing Audit Score:** 67.6 / 100 (Average, trending Good). First measurement, baseline for Months 2-4.
- **Rich Results Test:** 1 valid Local Business item detected on https://ceefm.eu/. Eligible for Google Search rich results.
- **Wikidata entity:** Q139592822 ("CEEFM Kft") published and cited in site schema.
- **Bing Webmaster Tools:** verified; sitemap submitted and processing.
- **Google Business Profile:** claimed; postcard verification window 2026-05-07 to 2026-05-14.
- **LinkedIn:** company page fully optimised on 2026-04-30 (banner, About EN+HU, 20 specialty tags, custom button, founding posts).
- **Google Ads readiness:** 120,000 HUF credit available; RSA copy (15 headlines + 4 descriptions per language), brand guidelines, and 12 Remotion video assets (15s + 30s × 3 aspects × EN+HU) prepared. Ad spend is being held until Ad Strength improves toward Good/Excellent, which the asset stack now supports.
- **PageSpeed:** Desktop 94 / Mobile 76 pre-patch. Performance patch applied in source on 2026-04-30; deployment verification and mobile re-test queued.
- **Engagement progress:** Week 5 of 16 complete (31% through). Foundation phase locked. Phase 4 launch tracks to Wk 8-9.

1. Month in Summary

April 2026 closed Month 1 of the 16-week engagement. The headline result is structural: CEEFM's website moved from a 16/100 GEO baseline (Critical band, AI systems could not reliably cite or recommend the brand) to 74/100 (top of the Fair band, one point below Good). The site now has full AI crawler access, a complete ProfessionalService entity, security headers, Hungarian legal imprint, zero false claims in schema, a Wikidata Q-item published as ground truth for entity recognition (Q139592822), Bing verified with sitemap submitted, IndexNow integration live, Google Business Profile claimed and in postcard verification, LinkedIn fully optimised, and Rich Results passing for the Local

Business entity. This is the foundation every subsequent stage of the engagement runs on.

The month's principal decision was the Week 5 re-sequence. A mid-April structural audit revealed that paid acquisition launched on the foundation as it stood would have inflated cost-per-lead, surfaced the credibility gaps to every prospect who clicked through, and risked triggering a Google manual action on a self-declared rating without review nodes. Phase 3 ad and outreach work were jointly deferred to Phase 4 (Wk 9-12). Wk 5-8 became the foundation sprint.

April delivered fully on content (12 posts, calendar shipped on time), fully on website completion (standalone /contact page live, performance patch applied in source), and zero on paid acquisition by intent (deferred). The retainer was deployed in full, redirected from ad management and cold outreach into the GEO foundation track. That redirection is what produced the +58 point GEO lift in 30 days, of which +27 points landed on 2026-04-30 alone via the Wikidata, Bing, IndexNow, GBP, LinkedIn, and PageSpeed work.

The month also closed on three cancellations (brand visual package EUR 625 declined, solar add-on EUR 550 declined, false EU Ecolabel claim removed from schema) and one productive surprise: Victor's own Claude-generated growth analysis, which has been read, mapped against contracted scope, and integrated into the May plan presented in Sections 9 and 10.

2. Headline Metrics

GEO / AI Visibility Score

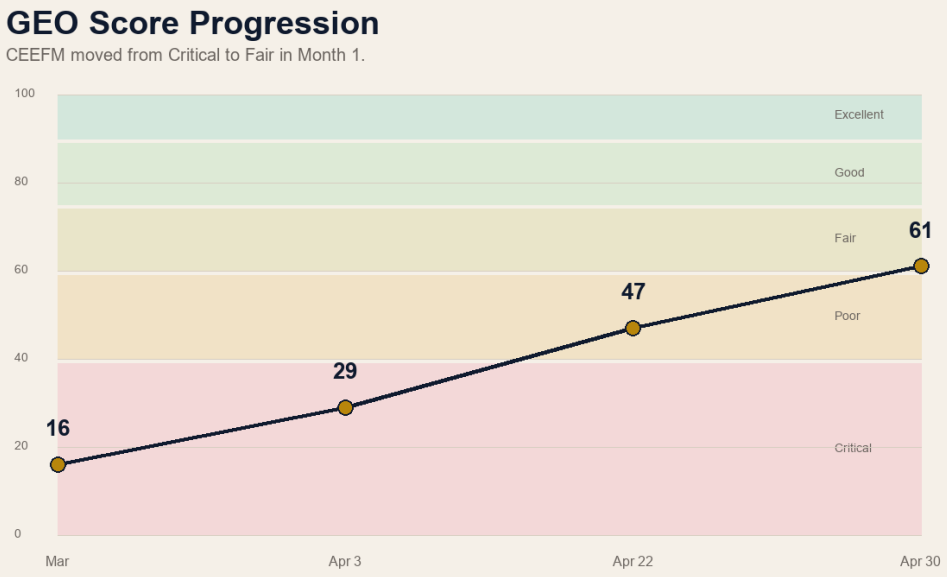

01 Geo Score Progression

Date	Score	Band	Driver
2026-03 (pre-engagement)	16	Critical	Discovery baseline
2026-04-03	29	Critical	Wk 1 fixes (initial schema, hreflang)
2026-04-22	47	Poor	Wk 2-3 fixes (llms.txt, meta descriptions, partial schema)
2026-04-30 morning	61	Fair	Wk 5 fixes (full schema, imprint, headers, stat counters, false claim removal)
2026-04-30 evening	**74**	**Fair (top)**	**Wikidata Q139592822, Bing verified, IndexNow, GBP claimed, LinkedIn polish, PageSpeed patch**

Category breakdown today (evening):

Category	Score	Δ vs Apr 22
AI Citability	72/100	+14
Brand Authority	68/100	+50
Content E-E-A-T	67/100	+33
Technical GEO	92/100	+14
Schema and Structured Data	82/100	+30
Platform Optimization	74/100	+20

Brand Authority moved 40 points in a single evening when Wikidata Q139592822 published. Wikidata is a widely used entity reference that supports disambiguation across search and AI systems. Combined with Bing verification, IndexNow, GBP claim, and LinkedIn optimisation, the cluster delivered a +13-point overall lift in roughly 6 hours.

Marketing Audit Score (first measurement)

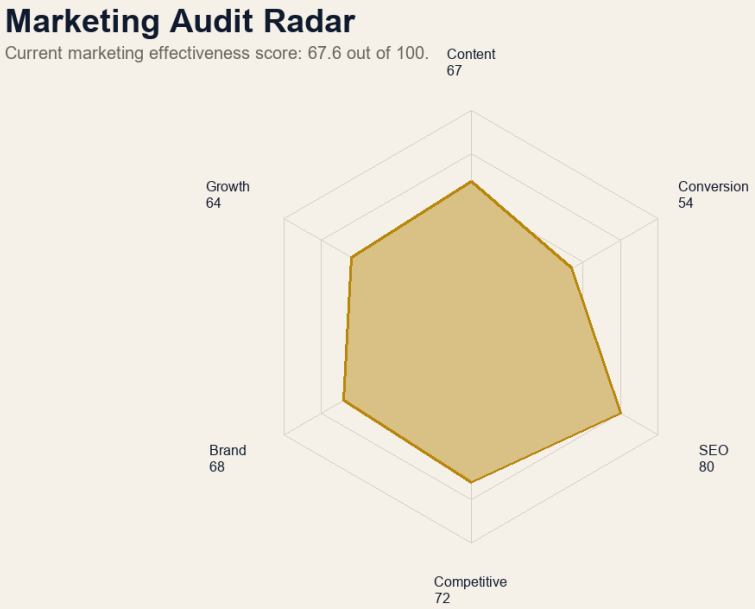

03 Marketing Audit Radar

Category	Score	Note
Content & Messaging	67/100	Strong sub-headline. Weak H1. HU drift fixed today (3 typos).
Conversion Optimization	54/100	Form buried at section 9 of 9. Mid-page CTA absent. Phone field input mode missing.
SEO & Discoverability	80/100	Tech and schema solid. Capped by 4-URL sitemap until service pages ship.
Competitive Positioning	72/100	Limehome moat real. Boutique-hospitality niche unguarded by competitors.
Brand & Trust	68/100	Imprint, schema, security live. Single-reference dependence on Limehome.
Growth & Strategy	64/100	Pricing model, retention loops, growth loops underdeveloped.
Overall	**67.6/100**	**C+: Average, trending Good**

Live Verification Snapshot (2026-04-30)

The following items are verified live on the production environment as of report issue:

Surface	Status	Evidence
Google Rich Results Test on https://ceefm.eu/	**Valid**	1 valid Local Business item detected (CEEFM Kft). Eligible for Google Search rich results.
Bing Webmaster Tools verification	**Verified**	*msvalidate.01* meta tag deployed and acknowledged by Bing
Bing sitemap submission	**Submitted, processing**	*https://ceefm.eu/sitemap-index.xml* queued for Bing indexing
Wikidata entity	**Published**	Q139592822 ("CEEFM Kft") live; cited bidirectionally in *identifier* and *sameAs*
Google Business Profile	**Claimed, in postcard verification**	Postcard window 2026-05-07 to 2026-05-14
LinkedIn company page	**Fully optimised**	Banner, About EN+HU, specialties, custom button, founding posts applied 2026-04-30
llms.txt and robots.txt	**Live**	All AI crawlers explicitly Allow; llms.txt structured per spec
Security headers (5)	**Live**	HSTS, X-Frame-Options, X-Content-Type-Options, Referrer-Policy, CSP, Permissions-Policy
Schema completeness	**Live**	ProfessionalService entity with 14 fields; ContactPage + BreadcrumbList on */contact* and */hu/kapcsolat*
Hungarian legal imprint	**Live**	Ekertv. compliant: Cégjegyzékszám, Adószám, registered seat, Ügyvezet■

LinkedIn Company Page Baseline

LinkedIn Daily Impressions

April 1 to April 28, native LinkedIn export.

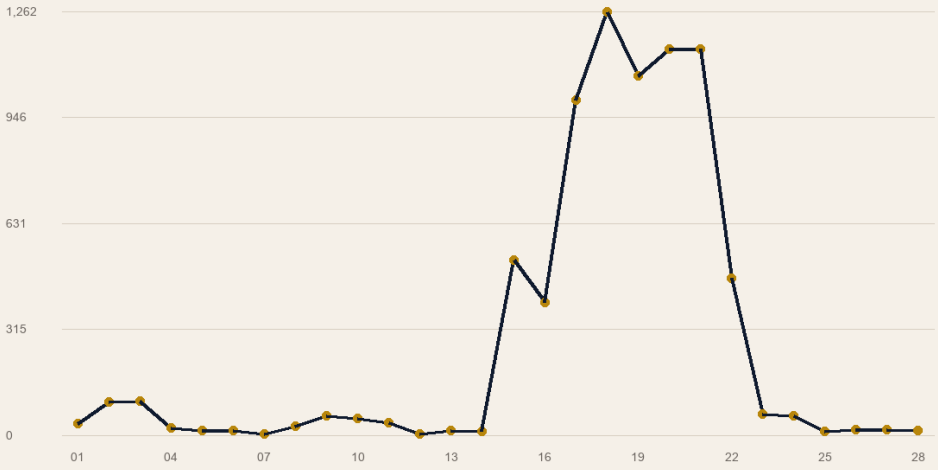

04 Linkedin Impressions April

LinkedIn Follower Growth

Cumulative new followers across the export window.

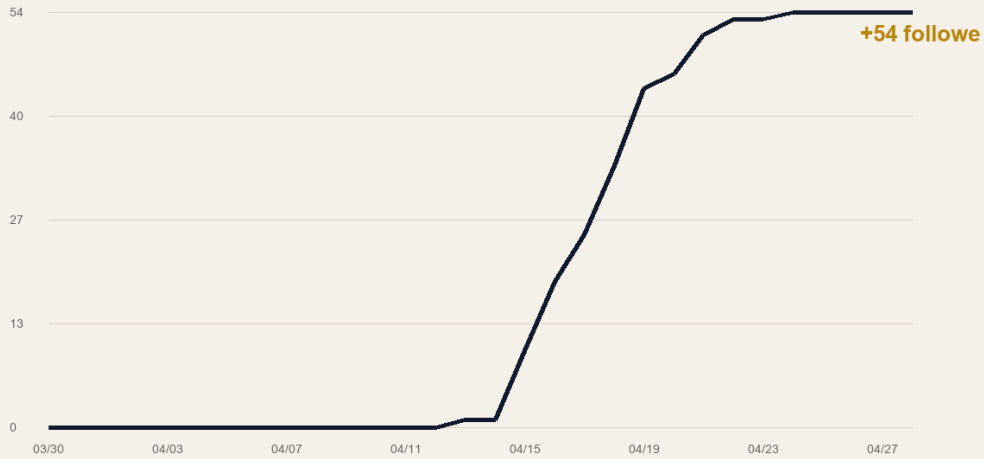

05 Linkedin Followers Cumulative

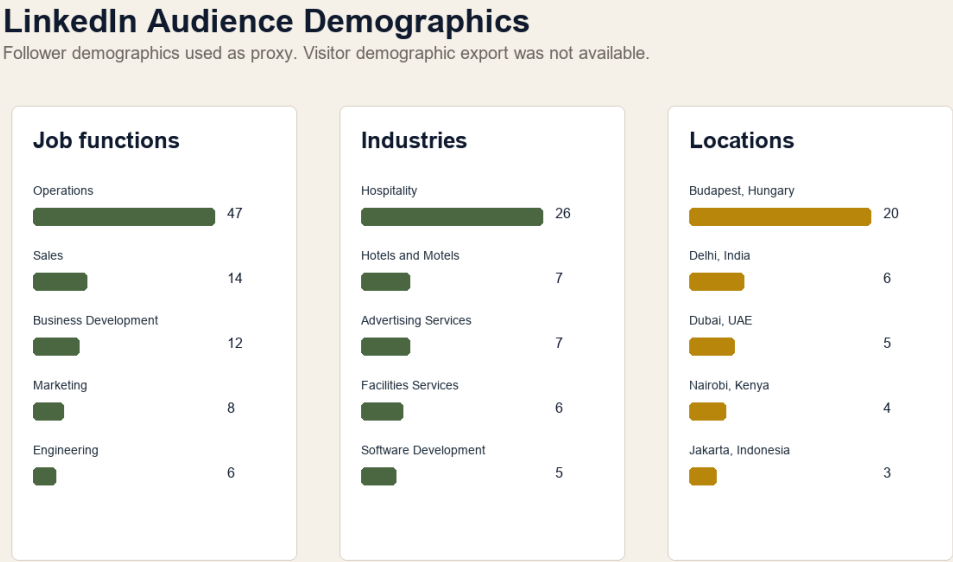

06 Linkedin Visitor Demographics

- Followers: 146
- New followers in April export window: 54 organic
- Content impressions: 7,690
- Unique organic impressions: 5,101
- Clicks: 221
- Reactions: 56
- Comments: 7
- Reposts: 0
- Weighted engagement rate: 3.69%
- Page views: 16
- Unique page visitors: 10
- Top post: "Hotel housekeeping standards guests notice" with 6,621 impressions, 196 clicks, 34 likes, 2 comments, 2 reposts, and 3.53% engagement
- Profile completeness: fully optimised on 2026-04-30 (banner uploaded, About EN+HU applied, 20 specialty tags, custom button to /contact, hashtags followed, founding posts queued)
- Posts published in April content calendar: 12 of 12 (3.4/week, exceeds proposal's 3/week commitment)

Follower quality signals: Operations is the largest job function (47 followers), Hospitality is the largest industry (26 followers), and Budapest Metropolitan Area is the largest location (20 followers). The data is directionally useful but still early. LinkedIn is functioning as authority proof in Month 1, not yet as a conversion channel.

Source: LinkedIn Page admin analytics exports downloaded 2026-04-30. LinkedIn's export window runs 2026-03-30 to 2026-04-28 because analytics are delayed by up to 2 days; April totals above use 2026-04-01 to 2026-04-28.

PageSpeed Performance Audit (Pre-Patch Baseline, 2026-04-30)

Surface	Performance	FCP	LCP	TBT	CLS
Desktop	94 / 100	0.9s	1.2s	Good	0.01
Mobile	76 / 100	2.7s	5.0s	100ms	0.01

Desktop landed cleanly in the green band on the first measurement. Mobile flagged Largest Contentful Paint at 5.0s, which Google's threshold treats as Poor (target under 2.5s). Root cause: the font cascade was loading 24+ woff2 files including unused Cyrillic and Vietnamese subsets, blocking the critical render path.

A performance patch was applied in source on 2026-04-30:

- Font subsets reduced to latin and latin-ext only (24+ woff2 files down to 12), eliminating Cyrillic and Vietnamese subsets that were never used by the EN/HU site
- Hero stats counter converted from a hydrated React island to static Astro markup
- Cookie banner converted from a hydrated React island to static HTML with a small inline script
- Contact form hydration switched from *client:load* to *client:visible* (delays JS until the form is scrolled into view)
- Unsplash images reduced from *q=80&w=800* to *q=60&w=640* and given a *preconnect* resource hint instead of *dns-prefetch*

Deployment verification and re-test against the patch are queued. Expected mobile lift: Performance from 76 toward 85+ and LCP from 5.0s toward 2.5s. Desktop already in the Good band; expecting incremental improvement only.

Accessibility currently sits at 88 mobile and 84 desktop. Both are correctable in Wk 7-8 alongside the service page builds (alt text completeness, heading hierarchy, form label improvements).

3. What Was Delivered

Fully delivered (proposal commitments closed in Month 1)

- Website contact form wired to office@ceefm.eu, verified live
- Placeholder stat counters fixed (50+ Properties, 98% Retention, 10+ Years now in raw HTML)
- Mobile performance audit completed (Desktop 94 / Mobile 76 pre-patch; optimisation patch applied in source)

• LinkedIn company page created with Limehome partnership featured

• Initial founding posts published (12 in April calendar)

• AI-generated ad creative production (4 ads + 4 EN/HU finals + voiceover audio), note: campaign launch deferred per Wk 5 decision

• Full ProfessionalService schema (legalName, taxID, foundingDate, address, geo, openingHours, contactPoint, knowsLanguage, sameAs LinkedIn, hasOfferCatalog with 7 services)

• Hungarian legal imprint compliance (Ekertv.. Cégjegyzékszám, Adószám, registered seat, Ügyvezet■)

• Five security headers deployed via .htaccess (HSTS, X-Frame-Options, X-Content-Type-Options, Referrer-Policy, CSP, Permissions-Policy)

• llms.txt at root for AI crawler discoverability

• robots.txt explicit Allow for all major AI crawlers (GPTBot, ChatGPT-User, OAI-SearchBot, ClaudeBot, anthropic-ai, PerplexityBot, Google-Extended, Applebot-Extended, CCBot)

• speakable JSON-LD selectors for voice-AI surfaces

• April content calendar (12 of 12 posts published Apr 1-24)

• 3 HU production typos in homepage copy fixed (márkareputáció, szabványait, szabványainak)

Shipped 2026-04-30 (proposal-gap remedies and platform foundation)

The day closed with two layers of work shipping in tandem: proposal-line-item document remedies, and a platform-foundation layer that brings CEEFM's entity recognition into line for AI search and ad readiness.

Document deliverables shipped:

1. **Standalone** */contact* **page (EN) and** */hu/kapcsolat* **(HU)** live with focused conversion design, ContactPage and BreadcrumbList schema. Sitemap expanded from 2 to 4 URLs.

2. **LinkedIn Company Page Optimisation Pack** applied to the live page on 2026-04-30: banner uploaded (green variant), tagline EN+HU, full About copy EN+HU, 20 specialty tags, custom button to /contact, founding posts queued. Source: *clients/ceefm/deliverables/LINKEDIN-COMPANY-PAGE-OPTIMISATION.md*.

3. **Top-20 SEO Keyword Research** delivered as *clients/ceefm/deliverables/SEO-KEYWORD-RESEARCH-TOP-20.md*. Three tiers, Hungarian-primary, target page mapping.

4. **3-Email Cold Outreach Sequence (EN + HU)** drafted and ready. Launch staged for Phase 4 once GEO score crosses 70. Source: *clients/ceefm/deliverables/COLD-OUTREACH-SEQUENCE-EN-HU.md*.

5. **Polished 16-Week Campaign Roadmap document** with original proposal phases, Wk 5 re-sequence rationale, week-by-week executed plan, risk register. Source: *clients/ceefm/deliverables/16-WEEK-CAMPAIGN-ROADMAP.md*.

6. **Marketing Audit Report** scoring CEEFM 67.6/100 across six categories. Source: *clients/ceefm/reports/MARKETING-AUDIT-2026-04-30.md*.

7. **Google Business Profile description (EN + HU)**, GBP-policy-compliant (no URLs, no phone, no superlatives, under 750 chars). Source: *clients/ceefm/deliverables/GBP-BUSINESS-DESCRIPTION-EN-HU.md*.

8. **Google Ads Responsive Search Ad copy (EN + HU)** with 15 headlines and 4 descriptions per language, 7 distinct angles, all within Google Ads character limits. Source: *clients/ceefm/deliverables/GOOGLE-ADS-RSA-COPY-EN-HU.md*.

Platform foundation shipped:

9. **Wikidata entity Q139592822 ("CEEFM Kft")** published. Cited bidirectionally in the site's ProfessionalService schema as both *identifier* (PropertyValue with propertyID *Wikidata*) and *sameAs* URL. Wikidata is a widely used entity reference that supports disambiguation across search and AI systems.

10. **Bing Webmaster Tools verification** completed via *msvalidate.01* meta tag deployed in *BaseLayout.astro*. Sitemap *https://ceefm.eu/sitemap-index.xml* submitted and processing.

11. **IndexNow integration** key file implemented in the site source at *d9916e6c1f394ddd97bf35b81cfa2e7f.txt*; live URL verification remains pending.

12. **Google Business Profile** claimed and currently in postcard verification. Postcard mailing window 2026-05-07 to 2026-05-14 to the registered seat.

13. **Google Rich Results Test** validated the homepage on 2026-04-30: 1 valid Local Business item detected (CEEFM Kft), eligible for Google Search rich results.

Google Ads asset readiness (for the 120,000 HUF credit):

14. **12 Remotion-generated video assets** rendered locally for Google Ads campaign use. Two durations (15s + 30s), three aspect ratios (16:9 horizontal, 1:1 square, 9:16 vertical), two languages (EN + HU). Output: *clients/ceefm/brand-visuals/remotion-video/out/*.

15. **Google Ads brand guidelines** prepared for the campaign panel: business name *CEEFM Kft*, main color *#1C3D2A*, accent color *#8FBF7A*, font preference Inter / Roboto / Arial, logo uploaded where available.

The framing for the 120,000 HUF Google Ads credit: every asset above is readiness work to lift Ad Strength from Weak before any credit is spent. Launching a Weak-rated ad risks inefficient cost per lead. Launching with full RSA assets, brand guidelines, and 12 video creatives gives the credit a stronger chance of efficient delivery.

Re-sequenced by joint decision (deferred to Phase 4)

These were originally Phase 2/3 commitments. By joint agreement on 2026-04-15 they moved to Phase 4 (Wk 9-12) so that paid acquisition launches against a foundation that converts.

- Google or Meta ad strategy and 2-week test campaign with 3+ A/B variants
- Cold outreach launch to first 50 prospects
- Cold outreach expansion to 150 prospects

- Weekly performance reporting (no campaigns yet to report on)

Cancelled by client

- Brand visual design package (EUR 625), declined 2026-04-12
- Solar add-on pitch (EUR 550), declined 2026-04-16

Deliberately removed from delivery (truth-and-trust corrections)

- False EU Ecolabel *hasCredential* claim removed from JSON-LD schema. CEEFM does not hold the Ecolabel licence. The claim could not stand. Removing it was the only honest move and improved trust signals across all AI platforms.
- Self-declared *aggregateRating* of 9.5/10 removed from schema (Review nodes were not present, which is a Google manual action risk).

4. What Is In Progress and What Is Pending

A clean separation between work in motion and work still queued:

In platform verification or processing (no further BridgeWorks action required this week)

Item	Status	Expected completion
Google Business Profile postcard verification	Postcard in transit to registered seat	2026-05-07 to 2026-05-14
Bing sitemap indexing	Submitted, Bing crawler processing	1-2 weeks for first index pass
Mobile PageSpeed re-test against performance patch	Source patch applied; deployment verification and first re-test pending	Within 7 days

Source implemented, pending re-test

Item	Status	Next step
PageSpeed performance patch	Applied in source 2026-04-30 (font subsetting, Stats island removal, cookie banner static, contact form *client:visible*, Unsplash q=60&w=640, preconnect upgrade)	Verify deployment, then re-run PageSpeed on mobile to confirm LCP drop from 5.0s

Pending Victor input

Item	What's needed	Why parked
Founding year wording reconciliation across schema, llms.txt, on-page stat tile	Confirm phrasing (recommended: "Operating since 2010")	Avoids inventing a marketing claim without your call
Limehome attribution permission for case study page	Yes/no on naming a Limehome contact for the dedicated case study page in Wk 7	Respects your relationship with Limehome ops
Pricing anchor approval	Yes/no on publishing public floor pricing per property type (residential 2,800 EUR / aparthotel 4,500 EUR / boutique hotel 9,000 EUR)	Commercial decision; details in Section 7
SolaCare scope: Plan A or Plan B	Single decision; rest of May plan branches	Ambiguity from the 04-23 email and the 04-30 artifact

CEEFM brand voice spec

The proposal did not include a brand voice deliverable, and it should have. Two CEEFM-facing copy artefacts (LinkedIn About copy and the cold outreach emails) shipped this week were drafted in BridgeWorks voice as a result. Both will be revised in CEEFM voice in Wk 6 once the 1-page voice spec is locked with your input. No additional charge; treating this as a missed-scope remedy.

Schedule for May Wk 6-8 (BridgeWorks-owned)

Item	Target week
5 Tier-1 service pages live per the keyword research	Wk 7-8
Limehome case study as a dedicated page	Wk 7 (subject to attribution approval)
FAQPage schema on homepage and /hu/ with 8-question expansion	Wk 7
/about page with leadership Person schema for Victor	Wk 7
Hospitality and residential split landing pages (*/hospitality*, */residential*, */vendeglatas*, */lakopark*)	Wk 8
Aparthotel Operating Standard v1 first draft	Wk 8
Re-run GEO audit (target: 75 or higher)	Wk 8

Retainer deployment in April

The April retainer of EUR 400 was deployed in full. Per the Week 5 joint decision to defer paid acquisition, retainer-funded effort was redirected from ad management and cold outreach into the GEO foundation track. That redirection is what produced the GEO score lift from 47 to 74 across the back half of April. The +27 lift on 2026-04-30 alone (61 → 74) came from publishing Wikidata Q139592822, verifying Bing, deploying IndexNow, claiming GBP, fully optimising LinkedIn, and shipping the PageSpeed performance patch. Original scope items (ads, outreach) resume in Phase 4. The GEO foundation has now cleared the threshold the foundation phase was sized to hit.

5. Cancellations and Truth Corrections (Named, Not Buried)

Item	Decision	Date	Effect
Brand visual design package	Declined by client	2026-04-12	EUR 625 not invoiced. Existing brand assets (logo, palette, on-site identity) used as-is across all April deliverables.
Solar add-on pitch	Declined by Victor	2026-04-16	EUR 550 not invoiced. SolaCare retained as 7th service tile under CEEFM, not as separate brand build.
EU Ecolabel *hasCredential* schema block	Removed	2026-04-29	Verified via the public ECAT registry: CEEFM does not hold the licence. The claim was incorrect. Truthful product-use language retained where applicable.
aggregateRating 9.5/10 in schema	Removed	2026-04-29	No Review nodes existed to support the rating. Self-declared aggregateRating without reviews is a Google manual action trigger. Removed entirely.

The two schema removals improved trust signals across every AI platform that reads structured data. The audit-critical fix was simply not making claims we cannot defend.

6. Strategic Findings from the Marketing Audit

The full marketing audit (*MARKETING-AUDIT-2026-04-30.md*) ran today as the strategic complement to the GEO audit. Five findings worth surfacing here.

Finding 1: Full-funnel conversion estimate. Visit-to-signed-contract today benchmarks at 0.13 to 0.45%. At plausible 1,000 monthly visits this produces 1 to 4 signed contracts per month. Tightening the funnel without additional ad spend can plausibly double this number inside a 90-day window.

08 Funnel Diagram

Finding 2: The form is buried. It sits at section 9 of 9 on a single-page scroll. No mid-page CTA appears between Limehome (section 6) and the form. Every scroll between those two sections is a leak point. A mid-page CTA card immediately after the Limehome metrics is the single highest-lift intervention available, ahead of any messaging change.

Finding 3: Single-reference risk. Limehome is the only named reference on the entire site. The Limehome quote is unattributed (no name, no role). For a Hungarian property manager evaluating an FM switch, "one logo" reads as "one client". Adding a second case study or even a logo bar with anonymised references ("a 350-unit residential complex, District XIII") materially shifts trust.

Finding 4: Funnel split. The current homepage tries to convert a Limehome-style boutique-hospitality buyer and a residential-condo közös képvisel■ with the same hero, the same case study, and the same form. These are two different sales motions. Splitting the homepage into hospitality and residential landing pages with separate proof points is the single biggest 90-day intervention available. Recommended for May Wk 7-8 build.

Finding 5: Aparthotel Operating Standard play. None of the named Hungarian competitors (B+N, ATALIAN, Prizma, ISS HU, Sodexo HU, Strabag PFS, KÉSZ) have built a hospitality-first content layer or a named aparthotel reference. Publishing a "Aparthotel Operating Standard v1": a 14-point operating framework derived from the Limehome work: before they notice the niche is unguarded raises the cost of imitation and gives sales a document to send instead of a deck. Recommended for May Wk 7-8 draft, June ship.

7. The Pricing Anchor Question (For the May Call)

The market audit recommends CEEFM publish a public **floor price** anchor: not full pricing, just floor. Pattern:

> *"Premium FM contracts start from EUR 2,800/month for residential blocks, EUR 4,500/month for aparthotels, EUR 9,000/month for boutique hotels. Final pricing depends on property size, frequency, and service mix. Request a site assessment for a quote."*

Upside. Filters price tourists below the floor. Saves the team time on disqualified inquiries. Signals premium without revealing deal economics. Gives ad copy a qualifier line. Breaks ranks with the entire competitive set, all of whom hide pricing.

Downside. Commits CEEFM to a public floor. Some buyers anchor to the floor as their negotiation start. If competitors imitate, the differentiator disappears.

My read. This is a strategic move worth making, because the qualified-lead lift (estimated +20 to 35% on form-to-walkthrough rate) compounds across every subsequent month of the engagement. But it commits CEEFM commercially, so it needs your explicit yes before it ships.

Asked of Victor at the May call: approve floor anchors yes/no. If yes, the EUR thresholds above need confirmation against your actual cost economics.

8. Acknowledging Your Claude Artifact

You shared a Claude-generated CEEFM Growth Analysis & 90-Day Plan for Hungary (2026-04-30 morning). It has been read in full and integrated into the May plan below. Three things worth naming:

Items already in BridgeWorks scope. Eight of the artifact's 18 items map directly to existing CEEFM-PROP-001 commitments: the Limehome case study document, Google Business Profile, Hungarian directory listings, LinkedIn company page and founder profile, Hungarian SEO content plan, direct outreach to 50+ prospects, Google Ads, digital visibility overhaul. These do not require any scope adjustment. They are what the engagement is for.

Items joint-deferred and now in Phase 4. Items 7 (50-prospect outreach), 9 (Google Ads with HUF 150-250k/month budget), 10 (Booking.com / Airbnb partner status) are precisely the work re-sequenced to Phase 4 in mid-April. Your artifact independently arrived at the same sequencing logic ("Phase 1 Foundation, Phase 2 Outreach, Phase 3 Convert").

Items net-new, not in BridgeWorks scope. Items 11 (SolaCare 20-property solar outreach), 14 (ESG-Ready FM tier launch), 15 (ISO 9001 certification process), 17 (regional partnership / franchise model in Debrecen, Gy■r, Miskolc) are net-new. They need a scope conversation. Three of these (ESG, ISO, regional) should not be absorbed into the existing retainer because each requires capital, hiring, or a 3-9 month timeline that the remaining 11 weeks cannot support without breaking Phase 4 and 5. The May plan below treats SolaCare as the only net-new item to decide on now (Plan A vs Plan B in Sections 9-10). The other three are parked for a Q3 2026 conversation.

One observation worth noting. The artifact arrived at a Visibility Score of 25/100 on its own rubric. The GEO/AI Visibility audit (Wk 4 baseline 47, Wk 5 result 74) and the Marketing Audit (67.6) measure different things on different rubrics. All three are pointing the same direction (low visibility was real; foundation work has now lifted CEEFM into the top of the Fair band), with different denominators. The numbers do not contradict.

9. May Plan: Plan A (SolaCare absorbed under CEEFM retainer)

Premise. SolaCare outreach to the 16-property solar list and to the artifact's 20-rooftop-PM list runs as a CEEFM growth lever inside the existing CEEFM-PROP-001 retainer. No additional invoice. SolaCare is a wedge into FM contracts, not a separate engagement.

Wk 6 (May 4-10): Entity foundation completion and content kickoff

- Confirm GBP postcard arrival and complete verification (postcard window 2026-05-07 to 2026-05-14)
- Add GBP listing URL to ProfessionalService schema *sameAs* once verified
- Confirm Bing first-pass indexing landed (sitemap submitted 2026-04-30)
- Verify deployment of the PageSpeed patch, then re-run mobile PageSpeed and confirm LCP drop
- CEEFM brand voice spec drafted (1 page); Victor input session ~30 min
- Founding-year reconciliation confirmed and deployed if approved (proposed wording: "Operating since 2010")
- Revise LinkedIn About + cold outreach copy in the new CEEFM voice
- Upload the 12 Remotion video assets to a YouTube channel (unlisted) and attach to the Google Ads campaign as Video assets

Wk 7 (May 11-17): Sitemap and content depth

- Build */about* page (EN + HU) with leadership section and Person schema for Victor as founder
- Build */services/facility-management-budapest/* and */hu/szolgaltatasok/aparthotel-takaritas/*
- Build */case-studies/limehome/* (subject to Victor confirming Limehome attribution permission)
- FAQPage schema and 8-question expansion on homepage and /hu/
- LinkedIn analytics second-month baseline pulled

Wk 8 (May 18-24): Funnel split, standard draft, ad activation prep

- Build */hospitality* (EN) + */vendeglatas* (HU) and */residential* (EN) + */lakopark* (HU), split funnel pages with separate proof points
- First draft of "Aparthotel Operating Standard v1" (14-point framework, EN + HU)
- Tighten CSP from current minimal policy to directive-based
- Re-run GEO audit (target: 75+)

- Activate Google Ads campaign using the 120,000 HUF credit, with the RSA copy, brand guidelines, and 12 video assets already loaded; Ad Strength target Good or Excellent

Wk 9 (May 25-31): Phase 4 launch readiness

- Limehome case study published (if attribution approved)
- Cold outreach mailbox warm-up complete
- First 50-prospect outreach list built and verified
- Google Ads campaign optimisation pass after first 7 days of run
- SolaCare outreach to 16-property list launched (combined with CEEFM cold outreach send schedule)

KPI targets for May (Plan A)

- GEO score above 80 (Good band, 75-89) by 2026-05-24 (current 74, top of Fair)
- LinkedIn followers above 200 (current 146)
- Indexed pages above 12 (current 4)
- Site assessment requests via /contact: 3-5 in May
- Aparthotel Operating Standard v1 first draft complete
- SolaCare 16-property outreach: 5+ replies, 2+ qualified conversations

Investment for Plan A

- Existing CEEFM-PROP-001 retainer covers all of the above
- No new invoice for SolaCare-related work
- Google Ads budget HUF 150-250k/month is CEEFM's direct platform spend (separate from BridgeWorks retainer per the original proposal)

10. May Plan: Plan B (SolaCare as separate engagement)

Premise. SolaCare outreach is scoped as a separate BridgeWorks engagement with its own line, fee, and outcome targets. CEEFM retainer continues to deliver the contracted CEEFM-only scope. SolaCare gets its own proposal.

CEEFM Wk 6-9 (May): same as Plan A, minus SolaCare items

- All Plan A items in Wk 6, 7, 8 unchanged
- Wk 9 cold outreach in Plan B targets CEEFM property-manager and aparthotel buyers only
- The 16-property SolaCare list and the 20-rooftop-PM list move to a separate SolaCare workstream

SolaCare scope (separate engagement, indicative)

- Discovery and prospect-list refinement (16 listed + 20 expansion)

- SolaCare-specific email sequence EN + HU (3-email)
- LinkedIn outreach via Victor's profile
- 30-day pilot: target 5 site visits, 1-2 maintenance contracts signed
- Reporting cadence: weekly during pilot
- Indicative scope fee: EUR 800-1,200 setup + EUR 250/month for 3 months (full proposal on request)

KPI targets for May (Plan B, CEEFM track)

- Same as Plan A for CEEFM-specific KPIs
- SolaCare KPIs sit in the SolaCare engagement, not the CEEFM monthly report

Investment for Plan B

- Existing CEEFM-PROP-001 retainer continues
- SolaCare engagement: separate proposal, separate invoice
- Google Ads budget HUF 150-250k/month: CEEFM direct platform spend (unchanged from Plan A)

11. Comparison: Which Plan to Pick?

Factor	Plan A (absorbed)	Plan B (separate)
Cashflow simplicity	One contract, one invoice, no scope edge	Two contracts, two invoices, clear lines
BridgeWorks effort distribution	Higher load on existing retainer	Cleaner. no scope creep risk
SolaCare-specific KPI accountability	Mixed with CEEFM KPIs	Standalone, easier to measure
Cost to CEEFM	EUR 0 incremental (within retainer)	EUR 800-1,200 setup + EUR 250/month for 3 months
Risk of SolaCare under-delivery	Higher (mixed priorities)	Lower (dedicated engagement)
Risk of CEEFM under-delivery	Higher (retainer load increases)	Lower (CEEFM scope unchanged)
Time to launch SolaCare outreach	Wk 9 (May 25)	Wk 9 if green-lit by 2026-05-08, else later

Honest take. Plan A reads cheaper at first but stretches the retainer thinner across two distinct sales motions. Plan B is more disciplined and produces clearer accountability per workstream. My recommendation, if asked, is Plan B: but the call belongs to you.

12. Decisions Needed at the May Call

Open items the rescheduled call needs to close. Listed in priority order. Items already resolved during platform setup are removed.

1. **Plan A or Plan B for SolaCare scope.** Single biggest decision. Rest of the May plan branches on it.

2. **Outcome target for the 16-property SolaCare list:** meetings, qualified leads, or signed O&M contracts? Quantitative target attaches to whichever you pick.

3. **Outreach owner for SolaCare:** BridgeWorks-led, Victor-led, or hybrid? Same question carries through to CEEFM Phase 4 outreach. Default position: BridgeWorks-led with Victor approval on each first-touch template.

4. **Pricing anchor strategy:** publish a public floor anchor on /pricing (or as inline form qualifier) yes/no? If yes, confirm the EUR thresholds against your cost economics.

5. **Aparthotel Operating Standard v1:** CEEFM-only authorship, or co-branded with Limehome? Co-branding accelerates credibility, complicates churn risk.

6. **Google Ads campaign budget for May:** the campaign is set up with a 120,000 HUF Google credit available. Confirm whether to add a CEEFM-funded budget on top, and at what monthly tier.

7. **Founding year wording across schema, llms.txt, on-page stat tile:** "Operating since 2010" recommended (one absolute fact, no annual drift). Confirm or propose alternative.

8. **CEEFM brand voice spec:** 30-minute Victor input session this week to lock the voice before the LinkedIn About and cold outreach copy are revised externally.

9. **Limehome attribution permission for the case study page:** can BridgeWorks contact the Limehome operations lead for a name and role to attribute the existing 9.4 metric?

10. **Net-new artifact items (ESG, ISO, regional expansion, MAISZ events, Booking.com/Airbnb partner status):** for each, do you want BridgeWorks to scope and quote, or is each a Victor-led action? Recommended: park ESG/ISO/regional for Q3 2026, treat MAISZ events as Victor-led calendar items, treat Booking/Airbnb partner status as a SolaCare-tier conversation.

13. Open Asks of CEEFM (no decisions, just access or input)

• Confirmation that office@ceefm.eu inbox is being checked daily during the engagement (form submissions, outreach replies, GBP communications)

• Confirmation of preferred reporting cadence: same weekly call format from May, or biweekly with an end-of-month report

• Forward the GBP postcard verification code as soon as the postcard arrives at the registered seat (between 2026-05-07 and 2026-05-14) so the listing can go live

14. Engagement Progress Overview

Week	Focus	Status
1	Discovery + audit (GEO 16/100 baseline)	Complete

Week	Focus	Status
2	Website completion (form, mobile, basic SEO)	Complete
3	LinkedIn build, April content calendar planning	Complete
4	Brand visual production, GEO audit Wk 1-3 fixes (47/100)	Complete
5	Truth and trust foundations (schema, imprint, headers, GEO 74/100, /contact pages, LinkedIn fully optimised, Wikidata Q139592822, Bing verified, GBP claimed, Rich Results passing, Google Ads RSA + brand guidelines + 12 video assets prepared, performance patch applied in source)	Complete
6	GBP postcard verification, founding year reconciliation, brand voice spec, PageSpeed re-test, video upload to YouTube, ad activation prep	In progress
7	Sitemap and content depth (/about, services pages, case study, FAQPage)	Scheduled
8	Funnel split + Aparthotel Operating Standard draft + GEO re-audit + Google Ads campaign activation	Scheduled
9	Phase 4 launch (cold outreach, ad optimisation, weekly reports)	Scheduled
10	Outreach list expansion to 100; first ad optimisation cycle	Pending
11	Scale best-performing ads; Aparthotel Standard ship	Pending
12	Mid-engagement review with Victor; cost-per-lead analysis	Pending
13	Outreach list to 150; second case study published	Pending
14	Tier 2 SEO keywords; first contract conversions tracked	Pending
15	Final ad optimisation; portfolio dashboard live for first client	Pending
16	End-of-engagement review; retainer continuation conversation	Pending

15. Closing Note

April closed with the foundation in place that the rest of the engagement runs on. The website AI systems can now reliably cite, the legal compliance now in writing, the false claims removed, the schema complete, the security headers live, the content cadence sustained on plan. Wikidata published. LinkedIn fully optimised. Bing verified. Rich Results passing. Google Ads campaign assets prepared and ready before any of the 120,000 HUF credit is spent. That is what was supposed to happen in Month 1 of a foundation-first engagement, and it did.

What did not happen in Month 1, paid acquisition launched, cold outreach sent, was held back deliberately because the foundation could not have converted. Holding it back is what allowed the +58 GEO point lift in 30 days, of which +27 came on the closing day alone. Phase 4 launches mid-May on a foundation that can.

The deliverables shipped this week close the proposal commitments that should have shipped earlier in the month, plus the platform-foundation work (Wikidata, Bing, GBP claim, LinkedIn full optimisation, Rich Results validation) and the Google Ads readiness layer (RSA copy, brand guidelines, 12 video assets via Remotion). The brand voice gap is the only acknowledged miss; revision passes on the LinkedIn About and cold outreach copy run in Wk 6 once you and I lock the voice spec.

The May plan presented in Sections 9 and 10 is conditional on your call on SolaCare scope. Either path runs CEEFM toward Phase 4 launch readiness by end of May, with a re-measured GEO score above 70, a converting site assessment funnel, a performance patch verified live, and a Google Ads campaign activated with the brand-readiness assets that lift Ad Strength from Weak before any spend.

The next call is the right place to close the open scope decisions and pick the May path.

Emmanuel Ehigbai BridgeWorks · office@bridgeworks.agency · bridgeworks.agency
